


**Work on the Coupar Angus Town Centre  
to start on 10th May 2010**

The Main Contractor: JKF (Group) Ltd.; intend to phase the works as shown on the adjacent drawing and an approximate timescale for each phase is listed below. PKC and JKF will inform residents of any changes to this programme.

- **Week 1 & 2** – Area 1 leading to area 2, pedestrian management in place to maintain public access
- **Week 3** – Complete area 2 leading on to both area 3 & 4, pedestrian management in place to maintain public access
- **Week 4** – Area 3 & 4, pedestrian management in place to maintain public access
- **Week 5** – Complete area 3 & 4 leading on to commence area 5, pedestrian management in place to maintain public access
- **Week 6** – Complete area 5 leading on to commence area 6, pedestrian management in place to maintain public access, requirement for 2-way traffic lights to provide working area on the carriageway
- **Week 7** – Complete area 6 leading on to commence area 8 & 10 i.e. traffic management 2-way lights increased length, pedestrian management in place to maintain public access
- **Week 8** – Area 7, pedestrian management in place to maintain public access, requirement for 2-way traffic lights to provide working area on the carriageway
- **Week 9** – Continue area 7 & commence area 9, i.e. traffic management 2-way lights increased length, pedestrian management in place to maintain public access
- **Week 10 (1st half)** – Complete areas 7 & 9 and commence area 11 i.e. traffic management 2-way lights increased length, pedestrian management in place to maintain public access
- **Week 10 (2nd half)** – Complete areas 7 & 9, continue area 11 and commence area 12, pedestrian management in place to maintain public access, road closure from mid-week say Wednesday 14/07/10
- **Week 11** – Complete area 11 & 12, complete road surface, road closure maintained through to completion i.e. 23/07/10

Please find below the Main contractors contact details should you need to contact them:

JKF (Group) Ltd, Quayside House,  
Dock Road, Methil Dock Business Park,  
Methil, Fife, KY8 3SR.  
Tel: 01333 424457

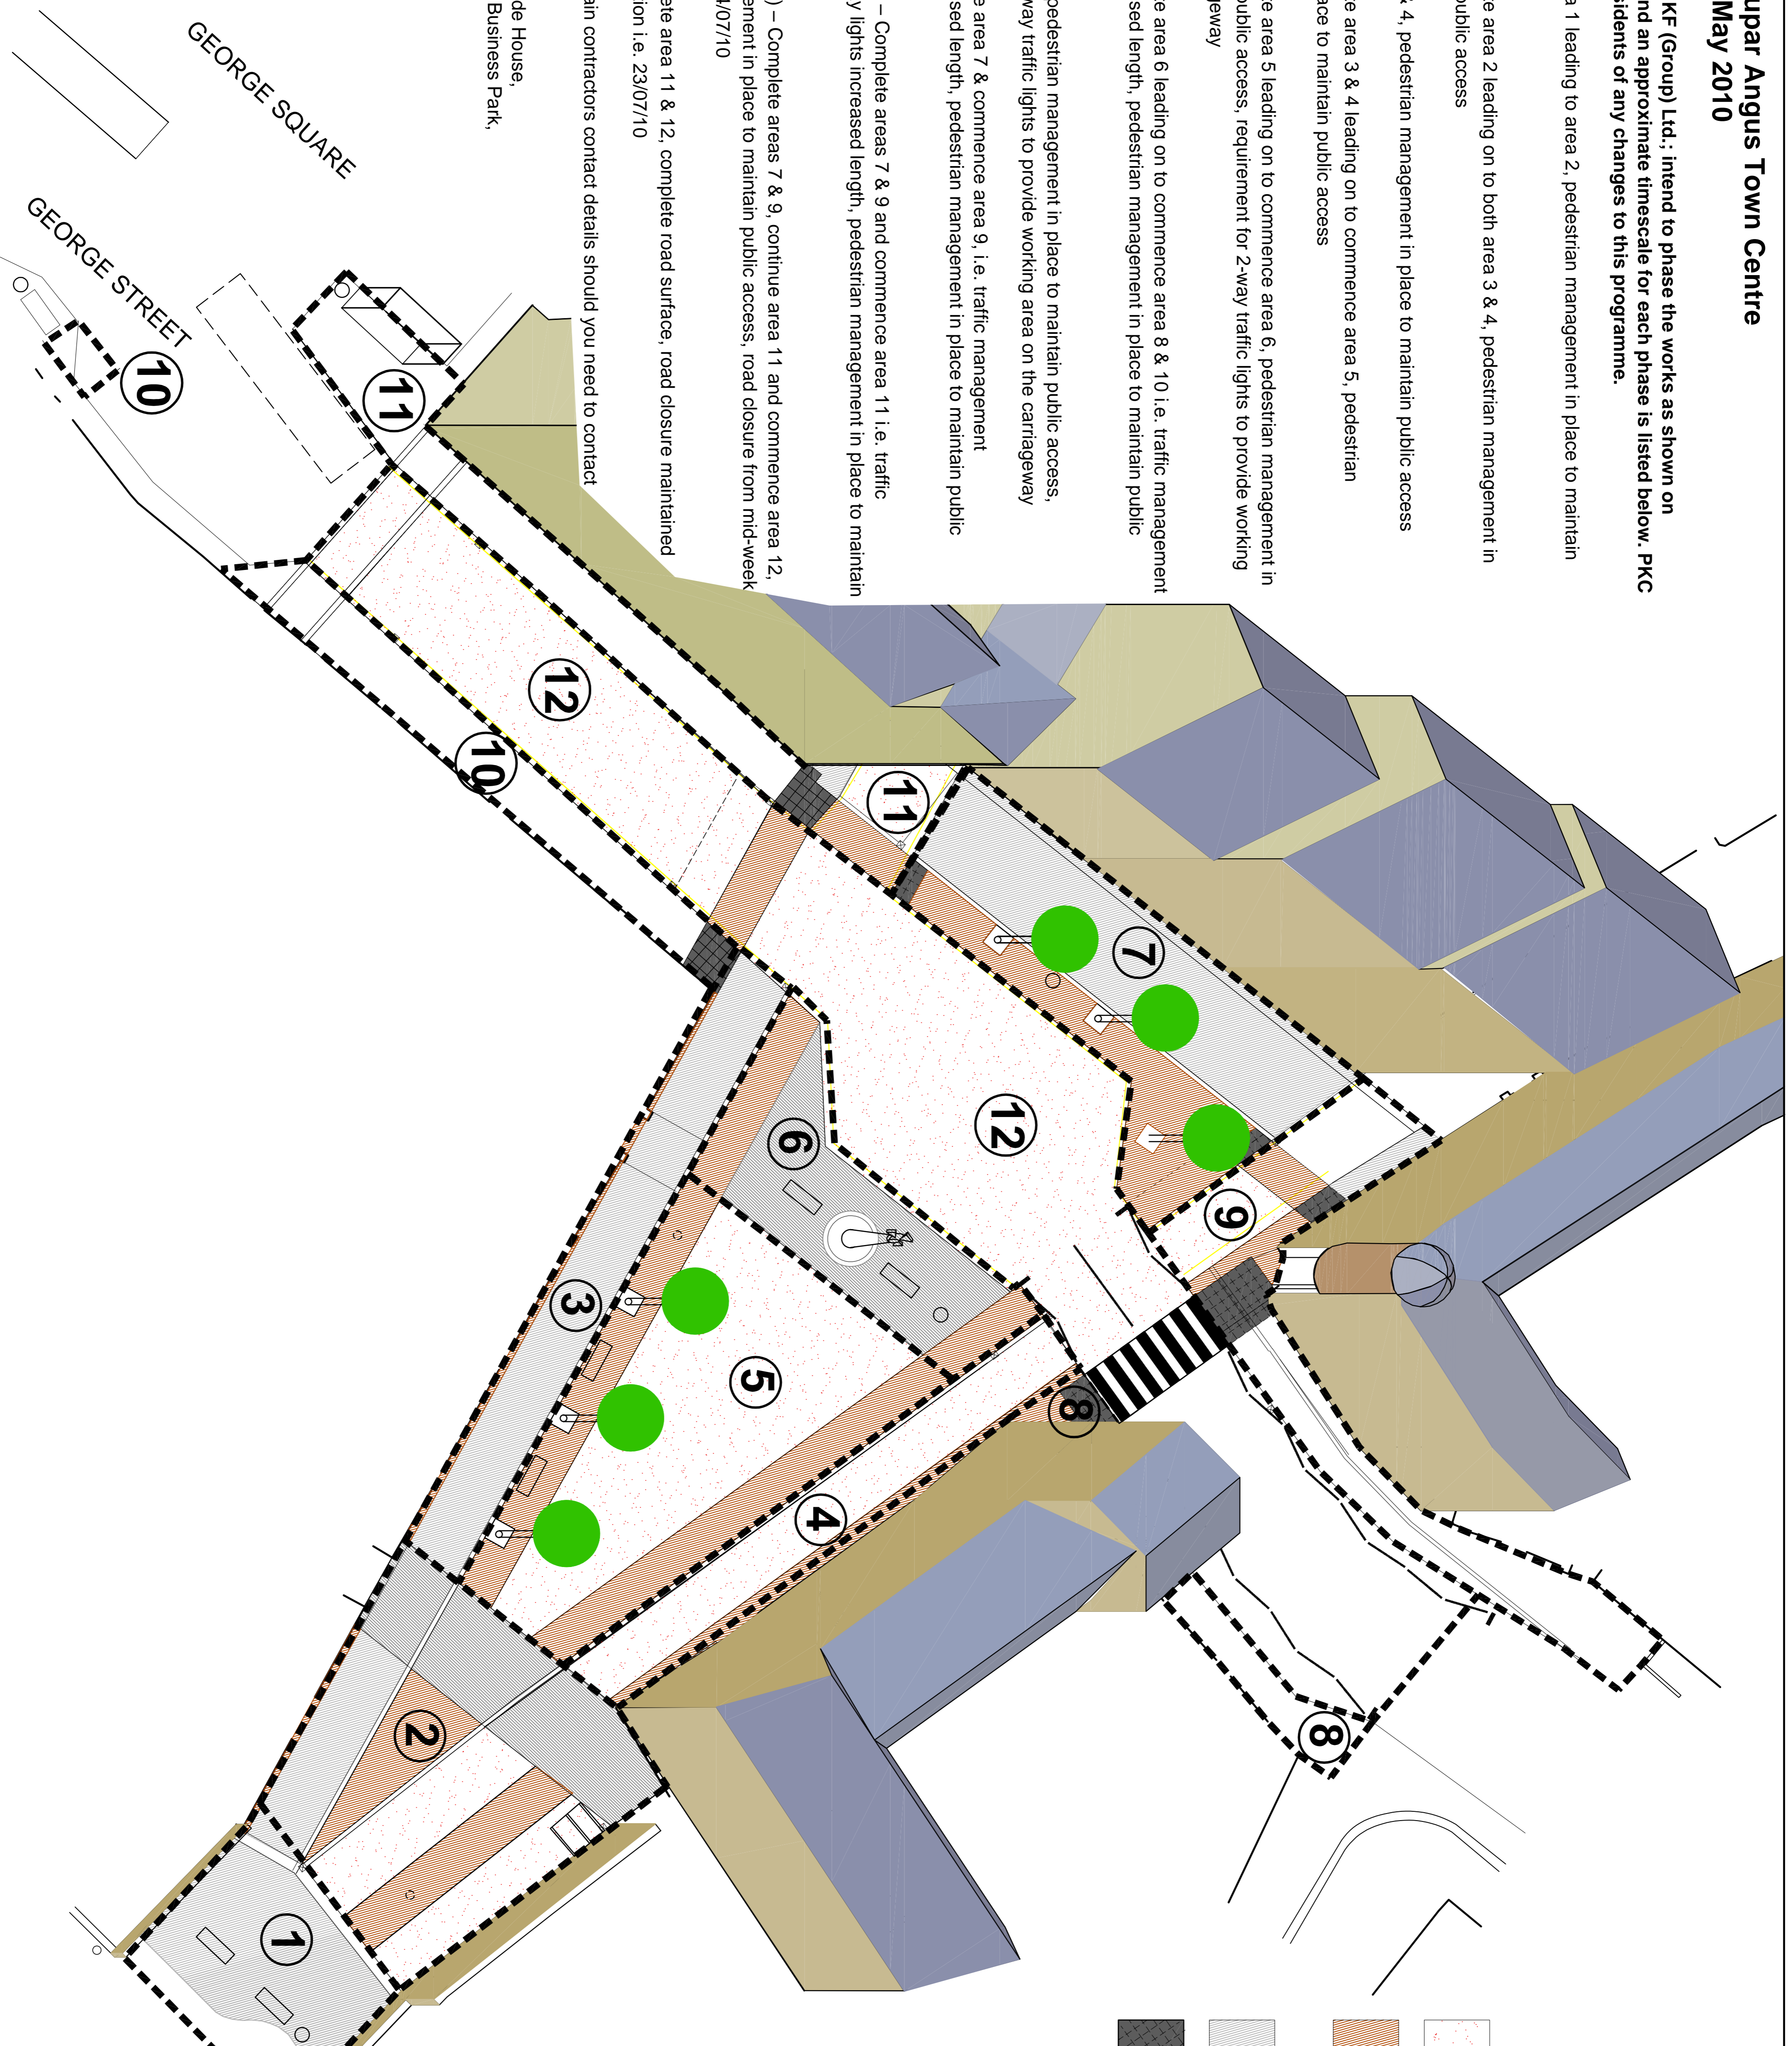


**Key:**

- Relocated existing lighting column
- Litter bin
- Bench
- Asphalt with red stone chip
- Red sandstone setts or similar to complement local building materials
- Courystone paving
- Charcoal coloured tactile paving
- ② Proposed JKF Work Area/Phase

Exact location of street furniture may vary

ALL DIMENSIONS ARE IN MILLIMETRES UNLESS OTHERWISE STATED. THE CONTRACTOR AND ANY SUBCONTRACTORS SHALL BE RESPONSIBLE FOR VERIFYING ALL DIMENSIONS AND ANY DISCREPANCIES SHOULD BE REPORTED TO THE PROJECT MANAGER BEFORE PROCEEDING.



**PERTH & KINROSS COUNCIL**  
LANDSCAPE SERVICES  
PILLAR HOUSE, 35 KINNOULL STREET, PERTH, PH1 5BP  
TEL: (01739) 476400

PROJECT: Coupar Angus Town Centre

TITLE: Plan showing Outline Proposals with Construction Phasing

SCALE:	1:150
DATE:	Sept '09
DRAWN:	DC
AUTH:	
REV:	
